

Maintenance Check List

Installatio	on Comp	oletion Date	: [0] 101	6
Address:	721	Germa	inder	

The following items have been provided and explained to the irrigation system owner or system owner's representative.

- The manufacturer's manual for the controller.
- A seasonal watering schedule.
- A list of components that require maintenance and the recommended frequency of maintenance is attached
- A permanent sticker has been attached to the controller indicating the warranty period for the irrigation system and contact information.
- The corrected or re-drawn design plans indicating the actual installation and components of the system.
- Location and operation of the isolation valve.

Irrigation system owner/representative

10|10|16 Date

This irrigation system has been installed in accordance with all applicable state and local laws, ordinances, rules, regulations or orders. I have tested the system and determined that it has been installed according to the irrigation plan and is properly adjusted for the most efficient application of water at this time.



Irrigator/Date

Irrigation Technician/ Date

## Best of Texas Landscapes


POBOX776 HUTTO, TX 78634 (512)228-4833 (512)852-9633 fax

Zone#	Description	Head Type	Run Time(Minutes)
1-2	bed	somu-bubbler	10-12
3-7	turf	SURVIS	25
8-11	TURC	rotors	45
12	ariss	drip	130
	<u> </u>		

Month	Average	
	Cycles	
Jan.	3	
Feb.	3	
March	4	
April	4	
May	7	
June	9	
July	11	
Aug.	11	
Sept.	9	
Oct.	6	
Nov.	4	
Dec.	3	

## MAINTENANCE ITEMS

Backflow device – Test Annually (Call Louis Sinclair 563-8762)
Y-strainer – Check annually for debris
Heads – Run system monthly to check for leaks or broken nozzles
Valve covers – Trim grass around cover to expose
Controller – Check seasonally for correct run times
Winter – Run system briefly every 2 weeks if system remains in off position

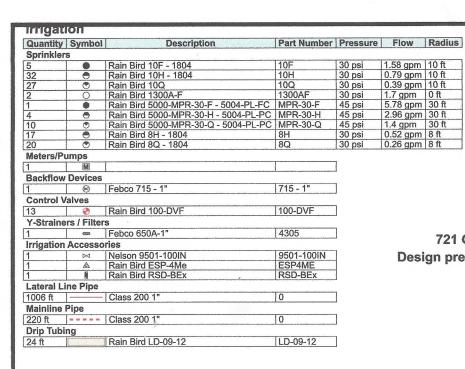

Water Source #1	
Meter Size	5/8 inch meter
Static Pressure	65 psi
Elevation Change	0 ft

Service Line Informati	on
Pipe Category	Class 200 PVC
Pipe Size	Class 200 1"
Length	5 ft
Velocity	5 fps

Recommendations	
Maximum Recommended Flow	13 gpm
Available Working Pressure	58.39 psi

**721 GERMANDER** Design pressure all zones 65psi.

1.58 gpm | 10 ft 0.79 gpm | 10 ft

0.39 gpm 10 ft 1.7 gpm 0 ft 5.78 gpm 30 ft

2.96 gpm 30 ft 1.4 gpm 30 ft 0.52 gpm 8 ft 0.26 gpm 8 ft

