

### COMPLETION ITEMS PROVIDED

- The manufacturer's manual for the controller.
- A seasonal watering schedule.
- A list of components that require maintenance and the recommended frequency of maintenance.
- A permanent sticker has been attached to the controller indicating the warranty period for the irrigation system and contact information.
- The corrected or re-drawn design plans indicating the actual installation and components of the system.
- Location and operation of the isolation valve.

### Recommended Run Times (minutes)


|                 |    |
|-----------------|----|
| • Spray – Shrub | 12 |
| • Spray – Lawn  | 25 |
| • Rotor – Lawn  | 45 |

### Recommended Monthly Cycles

| (Water Days) |    |
|--------------|----|
| • January    | 3  |
| • February   | 3  |
| • March      | 4  |
| • April      | 4  |
| • May        | 7  |
| • June       | 9  |
| • July       | 11 |
| • August     | 11 |
| • September  | 9  |
| • October    | 6  |
| • November   | 4  |
| • December   | 3  |

### Legend

- ⊙ DC Backflow
- ⊗ Control Valve
- Spray - Shrub
- Spray - Lawn
- ▼ Rotor - Lawn
- ▭ Drip Tubing
- - - Main Line

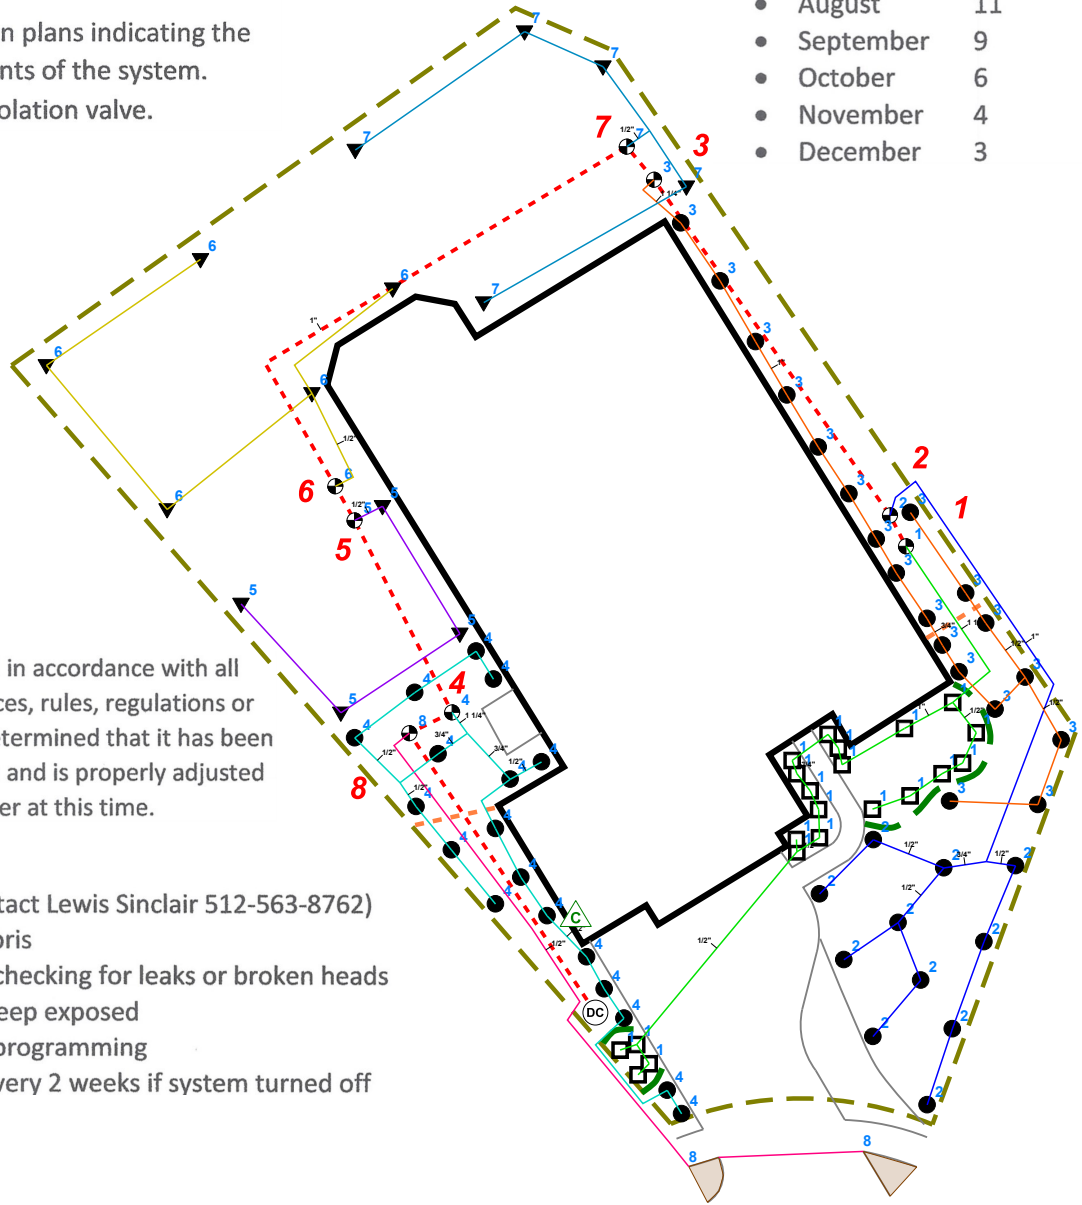

This irrigation system has been installed in accordance with all applicable state and local laws, ordinances, rules, regulations or orders. I have tested the system and determined that it has been installed according to the irrigation plan and is properly adjusted for the most efficient application of water at this time.

### Recommended Maintenance


- Backflow – Test Annually (contact Lewis Sinclair 512-563-8762)
- Filter – Check Annually for debris
- Heads – Run system monthly checking for leaks or broken heads
- Valve Covers – Trim grass to keep exposed
- Controller – Seasonal update programming
- Winter – Run system briefly every 2 weeks if system turned off

5100 ORSINI COVE



J

02/18/19

|                                                                                                                                                     |                                                                                                         |                                                                                                                                                                                                  |                                                                                                                                              |
|-----------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------|
| <p><b>REVISIONS:</b><br/>COMPLETION: 02/18/19</p>                                                                                                   | <p><b>PROJECT:</b><br/>5100 ORSINI COVE<br/>ROUND ROCK, TX 78665</p> <p>LOT 19, BLOCK O<br/>VIZCAYA</p> | <p><b>SHEET DESCRIPTION:</b><br/>IRRIGATION PLAN</p> <div style="text-align: center;">  <p>NORTH</p> </div> | <p><b>COMPANY:</b><br/>BEST OF TEXAS LANDSCAPES<br/>LIBERTY HILL, TEXAS 78642</p> <p>(512) 260-1430</p> <p>www.bestoftexaslandscapes.com</p> |
| <p><b>DATE:</b> 2019 - 02 / 01</p> <p><b>JOB NUMBER:</b> 78665-ORS-5100</p> <p><b>DRAWN BY:</b> SINCLAIR</p> <p><b>CHECKED BY:</b> STUBBLEFIELD</p> | <p><b>SCALE:</b> 1" = 20'</p> <p><b>SHEET:</b> 1 of 1</p>                                               |                                                                                                                                                                                                  |                                                                                                                                              |
