This irrigation system has been installed in accordance with all applicable state and local laws, ordinances, rules, regulations or orders. I have tested the system and determined that it has been installed according to the irrigation plan and is properly adjusted for the most efficient application of water at this time.

Recommended Maintenance

- Backflow Test Annually (contact Lewis Sinclair 512-563-8762)
- Filter Check Annually for debris
- Heads Run system monthly checking for leaks or broken heads
- Valve Covers Trim grass to keep exposed
- Controller Seasonal update programming
- Winter Run system briefly every 2 weeks if system turned off

COMPLETION ITEMS PROVIDED

- The manufacturer's manual for the controller.
- A seasonal watering schedule.
- A list of components that require maintenance and the recommended frequency of maintenance.
- A permanent sticker has been attached to the controller indicating the warranty period for the irrigation system and contact information.
- The corrected or re-drawn design plans indicating the actual installation and components of the system.
- Location and operation of the isolation valve.

Recommended Run Times (minutes)

Spray	y – Shrub	1

Spray – Lawn 25
Rotor – Lawn 45

<u>Legend</u>

(DC) Backflow

Control Valve

☐ Spray - Shrub

Spray - Lawn

▼ Rotor - Lawn

Drip Tubing

- - • Main Line





Recommended Monthly Cycles

(Water Days)

January

February 3

rebruary

March

April

4

May 7

June 9

July 11


August 11

September 9


October 6

November 4

December

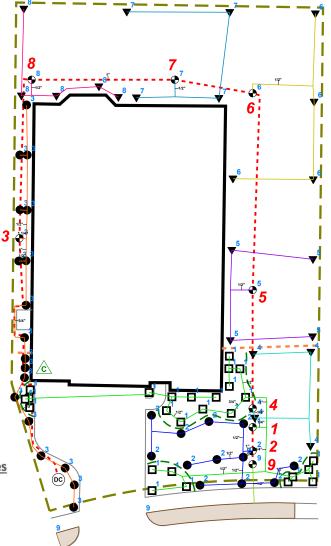

3112 DESERT SHADE BEND



PRO JECT

3112 DESERT SHADE BEND LEANDER, TX 78641

LOT 40, BLK V BLUFFS AT CRYSTAL FALLS



COMPANY

BEST OF TEXAS LANDSCAPES LIBERTY HILL, TEXAS 78642

(512) 260-1430

www.bestoftexaslandscapes.com
