This irrigation system has been installed in accordance with all applicable state and local laws, ordinances, rules, regulations or orders. I have tested the system and determined that it has been installed according to the irrigation plan and is properly adjusted for the most efficient application of water at this time.

## **COMPLETION ITEMS PROVIDED**

- The manufacturer's manual for the controller.
- A seasonal watering schedule.
- A list of components that require maintenance and the recommended frequency of maintenance.
- A permanent sticker has been attached to the controller indicating the warranty period for the irrigation system and contact information.
- The corrected or re-drawn design plans indicating the actual installation and components of the system.
- Location and operation of the isolation valve.

## Recommended Run Times (minutes)

- Spray Shrub 12
  Spray Lawn 25
- Rotor Lawn 45

### **Recommended Monthly Cycles**

# (Water Days)

- January
- February
- March
- April
- May
  7
- June 9

11


- July
- August 11
- September
- October
- .....
- November
- December 3

N STUBBLEFIE


# 07/13/19

### **Recommended Maintenance**

- Backflow Test Annually (contact Lewis Sinclair 512-563-8762)
- Filter Check Annually for debris
- Heads Run system monthly checking for leaks or broken heads
- Valve Covers Trim grass to keep exposed
- Controller Seasonal update programming
- Winter Run system briefly every 2 weeks if system turned off

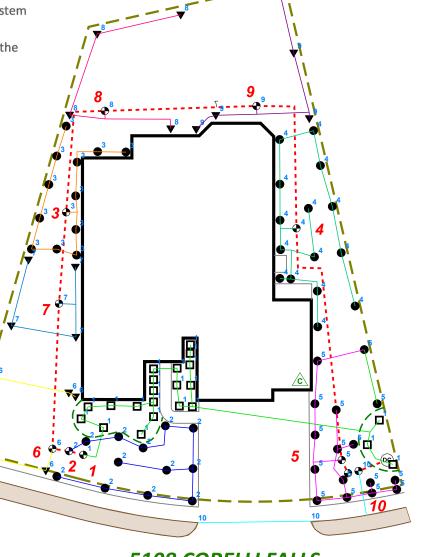

5108 CORELLI FALLS



### PROJECT

5108 CORELLI FALLS ROUND ROCK, TX 78665

LOT 1 BLK G VIZCAYA

Legend

**Backflow** 

**Control Valve** 

Spray - Shrub

Spray - Lawn

**Rotor - Lawn** 

**Drip Tubing** 

**Main Line** 



### COMPANY

BEST OF TEXAS LANDSCAPES LIBERTY HILL, TEXAS 78642

(512) 260-1430

www.bestoftexaslandscapes.com
