Date

This irrigation system has been installed in accordance with all applicable state and local laws, ordinances, rules, regulations or orders. I have tested the system and determined that it has been installed according to the irrigation plan and is properly adjusted for the most efficient application of water at this time.

COMPLETION ITEMS PROVIDED

- The manufacturer's manual for the controller.
- A seasonal watering schedule.
- A list of components that require maintenance and the recommended frequency of maintenance.
- · A permanent sticker has been attached to the controller indicating the warranty period for the irrigation system and contact information.
- The corrected or re-drawn design plans indicating the actual installation and components of the system.
- · Location and operation of the isolation valve.

Recommended Maintenance

- Backflow Test Annually
- Filter Check Annually for debris
- Heads Run system monthly checking for leaks or broken heads
- Valve Covers Trim grass to keep exposed
- · Controller Seasonal update programming
- Winter Run system briefly every 2 weeks if system turned off

Recommended Monthly Cycles

(Water Days) January February March April May June July 11 August September October

> November December


Recommended Run Times (minutes)

 Spray – Shrub Spray – Lawn 25 45 Rotor – Lawn

Drip – Lawn

Best of Texas Landscapes

1" = 20

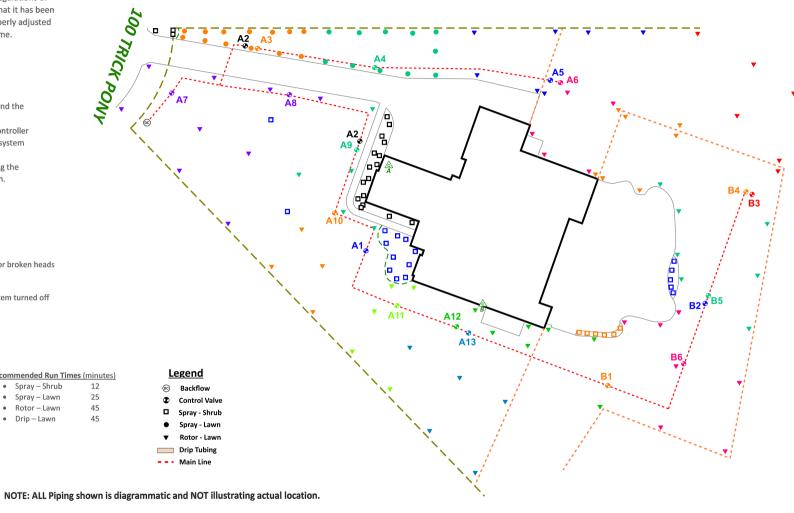

07/21/21

PROJECT: 100 TRICK PONY LIBERTY HILL TX 78642

LOT 48 BLK E CLEARWATER IRRIGATION PLAN



SHEET DESCRIPTION:

BEST OF TEXAS LANDSCAPES LIBERTY HILL, TEXAS 78642

COMPANY:

(512) 260-1430

www.bestoftexaslandscapes.com





06/21/2021
