

**Recommended Run Times (minutes)**

- Spray – Shrub 12
- Spray – Lawn 25
- Rotor – Lawn 45
- Drip – Lawn 45



**Recommended Monthly Cycles**


- (Water Days)
- January 3
  - February 3
  - March 4
  - April 4
  - May 7
  - June 9
  - July 11
  - August 11
  - September 9
  - October 6
  - November 4
  - December 3

**Recommended Maintenance**

- Backflow – Test Annually
- Filter – Check Annually for debris
- Heads – Run system monthly checking for leaks or broken heads
- Valve Covers – Trim grass to keep exposed
- Controller – Seasonal update programming
- Winter – Run system briefly every 2 weeks if system turned off

**Legend**

- ⊙ Backflow
- ⊗ Control Valve
- Spray - Shrub
- Spray - Lawn
- ▼ Rotor - Lawn
- Drip Tubing
- - - Main Line

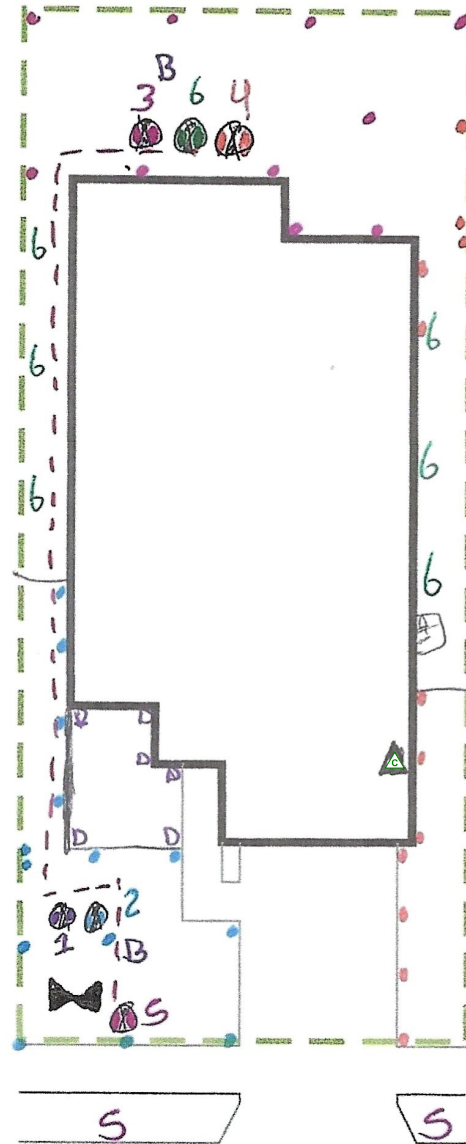

**COMPLETION ITEMS PROVIDED**

- The manufacturer's manual for the controller.
- A seasonal watering schedule.
- A list of components that require maintenance and the recommended frequency of maintenance.
- A permanent sticker has been attached to the controller indicating the warranty period for the irrigation system and contact information.
- The corrected or re-drawn design plans indicating the actual installation and components of the system.
- Location and operation of the isolation valve.

**110 CORN LANE**



*[Handwritten Signature]*

9.9.2024

This irrigation system has been installed in accordance with all applicable state and local laws, ordinances, rules, regulations or orders. I have tested the system and determined that it has been installed according to the irrigation plan and is properly adjusted for the most efficient application of water at this time.

\_\_\_\_\_  
System Owner / Representative

\_\_\_\_\_  
Date

**NOTE: ALL Piping shown is diagrammatic and NOT illustrating actual location.**

|                  |                    |                             |                           |                           |                   |                                       |   |   |  |
|------------------|--------------------|-----------------------------|---------------------------|---------------------------|-------------------|---------------------------------------|---|---|--|
| SHEET:<br>1 of 1 | SCALE:<br>1" = 20' | CHECKED BY:<br>STUBBLEFIELD | DRAWN BY:<br>STUBBLEFIELD | JOB NUMBER:<br>7834COR110 | DATE:<br>9/9/2024 | REVISIONS:<br>COMPLETION:<br>10/18/24 | PROJECT:<br>110 CORN LANE<br>HUTTO, TX 78634<br><br>LOT 15 BLOCK DD<br>HUTTO CROSSING | SHEET DESCRIPTION:<br>IRRIGATION PLAN<br><br> | COMPANY:<br>BEST OF TEXAS LANDSCAPES<br>LIBERTY HILL, TEXAS 78642<br><br>(512) 260-1430<br><br>www.bestoftexaslandscapes.com |
|------------------|--------------------|-----------------------------|---------------------------|---------------------------|-------------------|---------------------------------------|---|---|--|
