

1" = 20'

This irrigation system has been installed in accordance with all applicable state and local laws, ordinances, rules, regulations or orders. I have tested the system and determined that it has been

installed according to the irrigation plan and is properly adjusted

for the most efficient application of water at this time.

# **COMPLETION ITEMS PROVIDED**

- The manufacturer's manual for the controller.
- A seasonal watering schedule.
- A list of components that require maintenance and the recommended frequency of maintenance.
- A permanent sticker has been attached to the controller indicating the warranty period for the irrigation system and contact information.
- The corrected or re-drawn design plans indicating the actual installation and components of the system.
- Location and operation of the isolation valve.

#### **Recommended Maintenance**

- Backflow Test Annually (contact Lewis Sinclair 512-563-8762)
- Filter Check Annually for debris
- Heads Run system monthly checking for leaks or broken heads
- Valve Covers Trim grass to keep exposed
- Controller Seasonal update programming
- Winter Run system briefly every 2 weeks if system turned off

#### **Recommended Monthly Cycles**

(Water Days)

<ul><li>January</li></ul>	J
---------------------------	---

- February 3
- March
- April
- 7 May
- June 9
- July 11
- 11 August
- September 9
- October 6
- November 4
- December 3





#### Recommended Run Times (minutes)

•	Spray	– Shrub	12
---	-------	---------	----

25 Spray – Lawn

Rotor - Lawn 45

## Legend

**Backflow** 

**Control Valve** 


Spray - Shrub

Spray - Lawn

Rotor - Lawn

**Drip Tubing** 

**Main Line** 

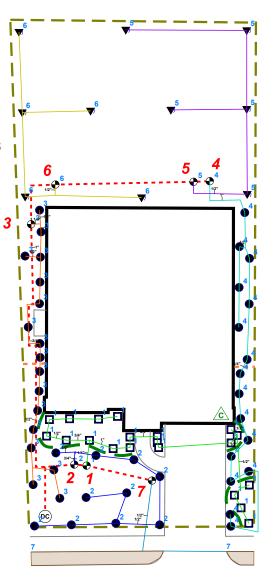

# 12930 MESA VERDE DRIVE



# 12930 MESA VERDE DRIVE AUSTIN, TX 78737

LOT 4, BLOCK A



BEST OF TEXAS LANDSCAPES LIBERTY HILL, TEXAS 78642

(512) 260-1430

www.bestoftexaslandscapes.com
