
1" = 20'

This irrigation system has been installed in accordance with all applicable state and local laws, ordinances, rules, regulations or orders. I have tested the system and determined that it has been installed according to the irrigation plan and is properly adjusted for the most efficient application of water at this time.

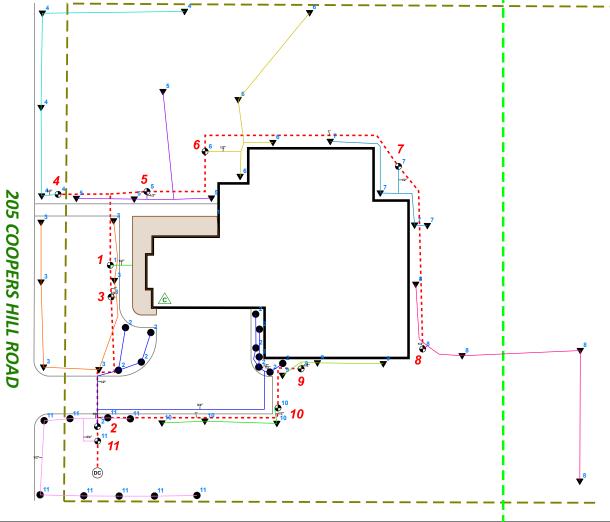

## **COMPLETION ITEMS PROVIDED**

- The manufacturer's manual for the controller.
- A seasonal watering schedule.
- A list of components that require maintenance and the recommended frequency of maintenance.
- A permanent sticker has been attached to the controller indicating the warranty period for the irrigation system and contact information.
- The corrected or re-drawn design plans indicating the actual installation and components of the system.
- Location and operation of the isolation valve.

#### **Recommended Maintenance**

- Backflow Test Annually (contact Lewis Sinclair 512-563-8762)
- Filter Check Annually for debris
- Heads Run system monthly checking for leaks or broken heads
- Valve Covers Trim grass to keep exposed
- Controller Seasonal update programming
- Winter Run system briefly every 2 weeks if system turned off

#### **Recommended Monthly Cycles**

	(Water Days)	
•	January	3
•	February	3
•	March	4
•	April	4
•	May	7
•	June	9
•	July	11
•	August	11
•	September	9
•	October	6
•	November	4
•	December	3

### **Recommended Run Times** (minutes)

- Spray Shrub 12 25 Spray - Lawn
- 45 Rotor - Lawn

# **Legend**



**Control Valve** 


Spray - Shrub

Spray - Lawn

Rotor - Lawn

**Drip Tubing** 

Main Line



205 COOPERS HILL ROAD GEORGETOWN, TX 78628

LOT 16 BLK I HEIGHTS OF GEORGETOWN



#### BEST OF TEXAS LANDSCAPES LIBERTY HILL, TEXAS 78642

(512) 260-1430 www.bestoftexaslandscapes.com



