

This irrigation system has been installed in accordance with all applicable state and local laws, ordinances, rules, regulations or orders. I have tested the system and determined that it has been installed according to the irrigation plan and is properly adjusted for the most efficient application of water at this time.

COMPLETION ITEMS PROVIDED

- The manufacturer's manual for the controller.
- A seasonal watering schedule.
- A list of components that require maintenance and the recommended frequency of maintenance.
- A permanent sticker has been attached to the controller indicating the warranty period for the irrigation system and contact information.
- The corrected or re-drawn design plans indicating the actual installation and components of the system.
- Location and operation of the isolation valve.

Recommended Maintenance

- Backflow Test Annually (contact Lewis Sinclair 512-563-8762)
- Filter Check Annually for debris
- Heads Run system monthly checking for leaks or broken heads
- Valve Covers Trim grass to keep exposed
- Controller Seasonal update programming
- Winter Run system briefly every 2 weeks if system turned off

Recommended Run Times (minutes)

Spray -	Shruh	12
JUIGV	JIIIUU	12

25 Spray – Lawn

Rotor – Lawn 45

Legend



Control Valve

Spray - Shrub

Spray - Lawn

Rotor - Lawn

Drip Tubing

Main Line





Recommended Monthly Cycles

3

3

4

7

9

11

9

6

4

3

(Water Days)

January

February

March

April

July

May

June


11 August

September

October

November

December

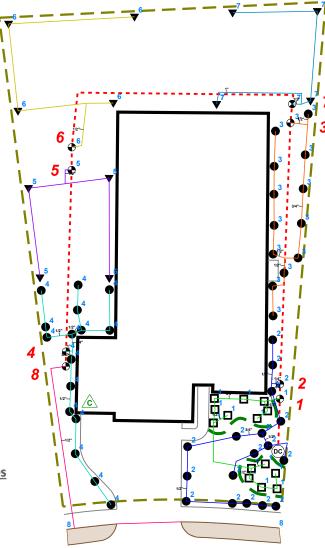

5105 CORELLI FALLS

07/28/19

5105 CORELLI FALLS ROUND ROCK, TX 78665

LOT 2, BLOCK P VIZCAYA



BEST OF TEXAS LANDSCAPES LIBERTY HILL, TEXAS 78642

(512) 260-1430

www.bestoftexaslandscapes.com
